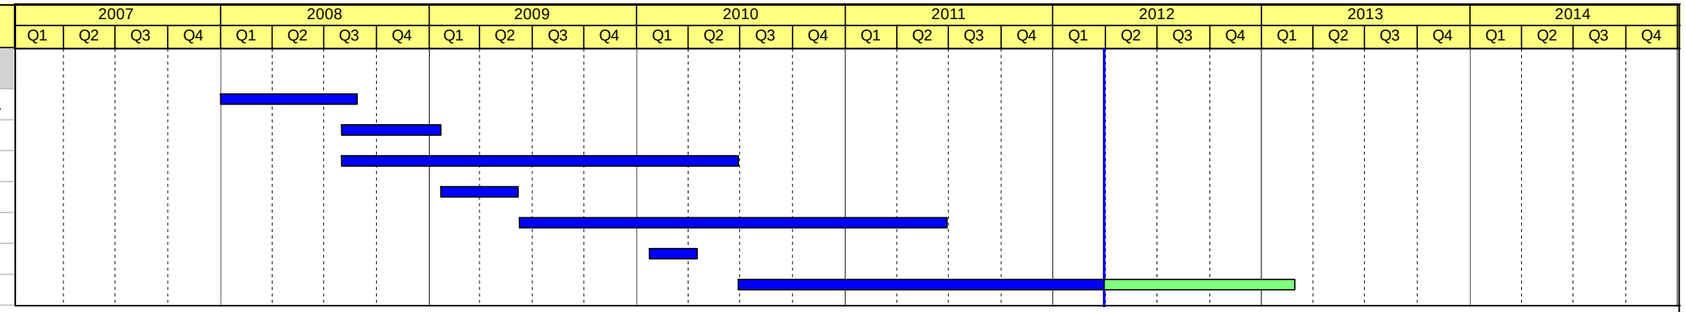Activity Name	Start	Finish
Johnnie Dodds Boulevard		
Concept Report	02-Jan-08 A	28-Aug-08 A
Preliminary Plans	01-Aug-08 A	22-Jan-09 A
Utility Coordination	01-Aug-08 A	28-Jun-10 A
ROW Plans	23-Jan-09 A	05-Jun-09 A
ROW Acquisition	09-Jun-09 A	30-Jun-11 A
Advertise for Bids	22-Jan-10 A	16-Apr-10 A
Construction	28-Jun-10 A	28-Feb-13
